



ANTICIPATED MAINTENANCE OF TRAFFIC

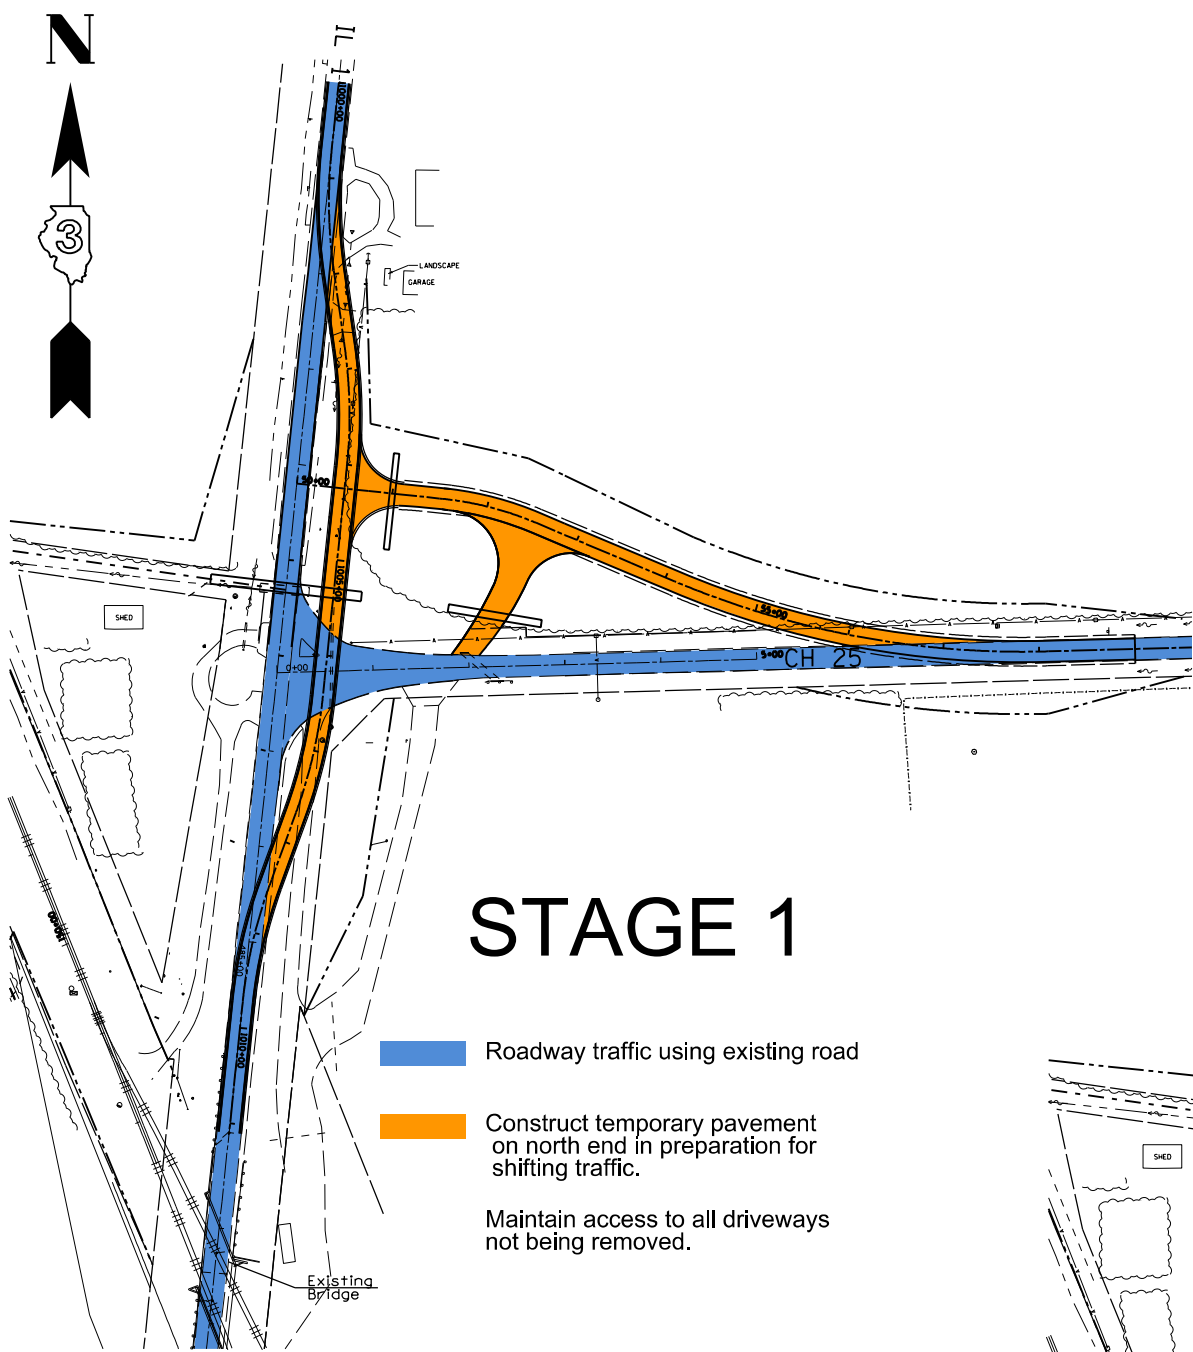


STAGE 1

- Roadway traffic using existing road
- Construct temporary pavement on north end in preparation for shifting traffic.
- Maintain access to all driveways not being removed.

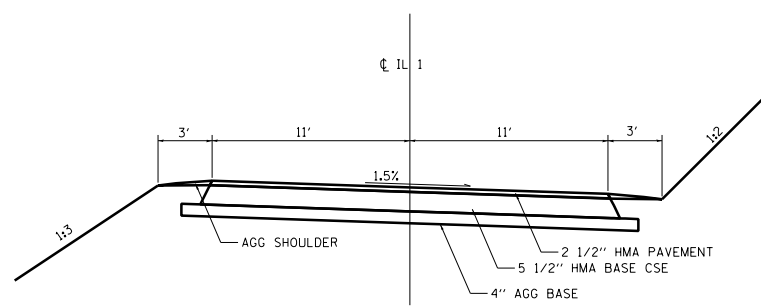


TEMPORARY PAVEMENT TYPICAL SECTION
STAGE 1

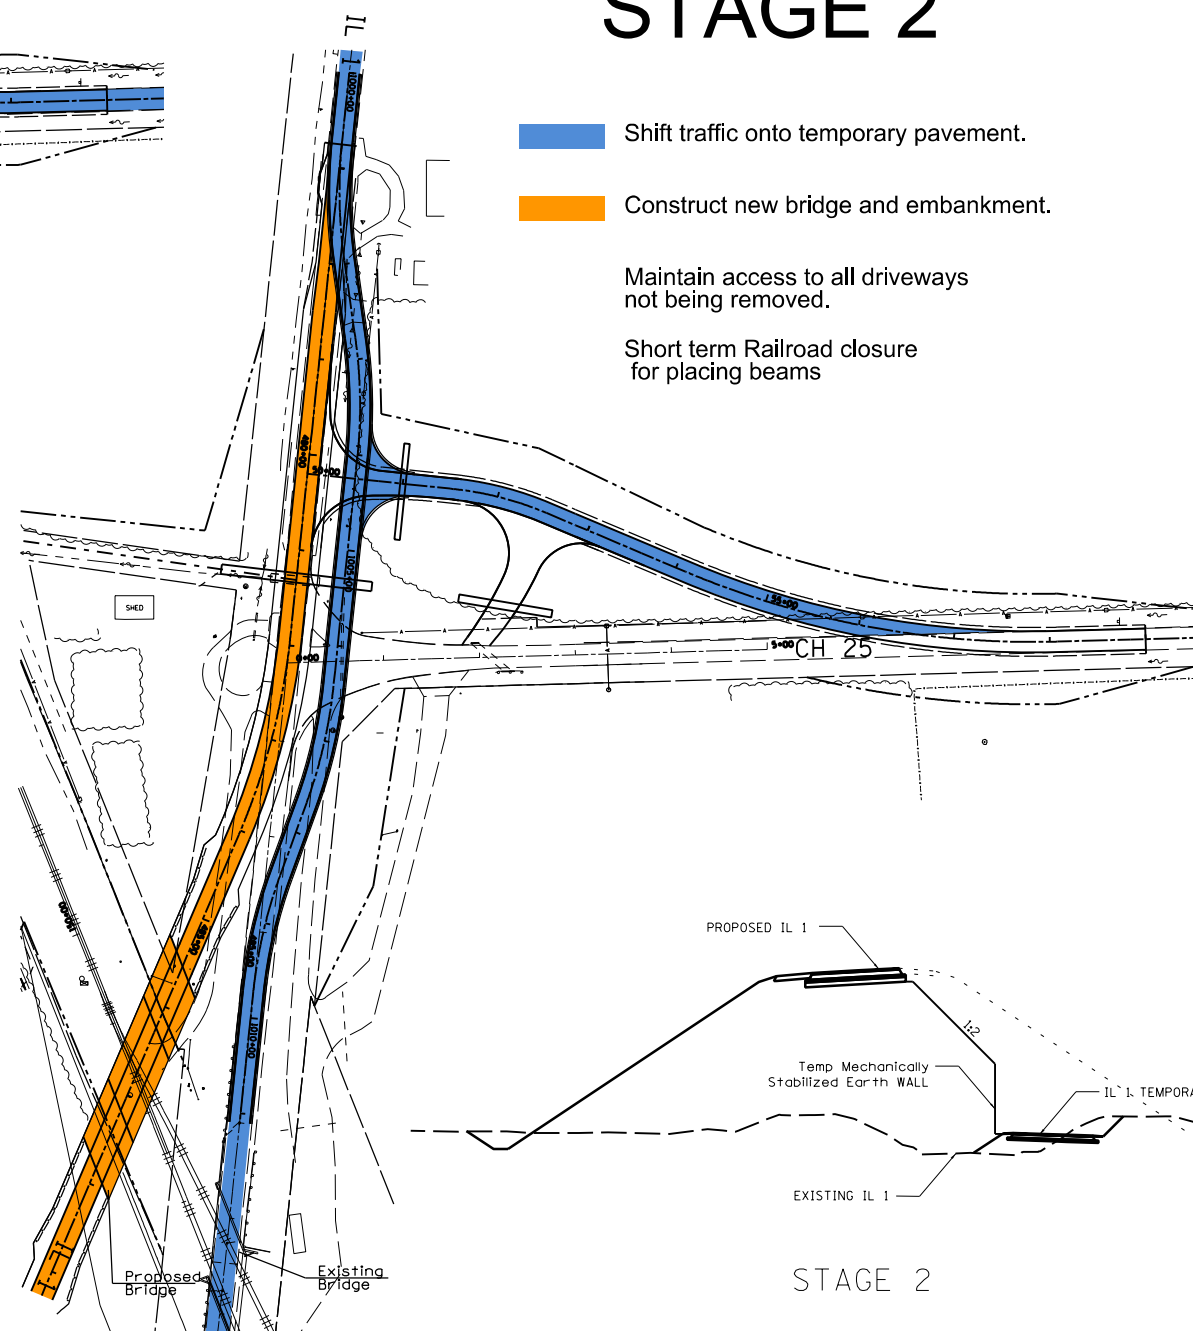


STAGE 2

- Shift traffic onto temporary pavement.
- Construct new bridge and embankment.
- Maintain access to all driveways not being removed.
- Short term Railroad closure for placing beams

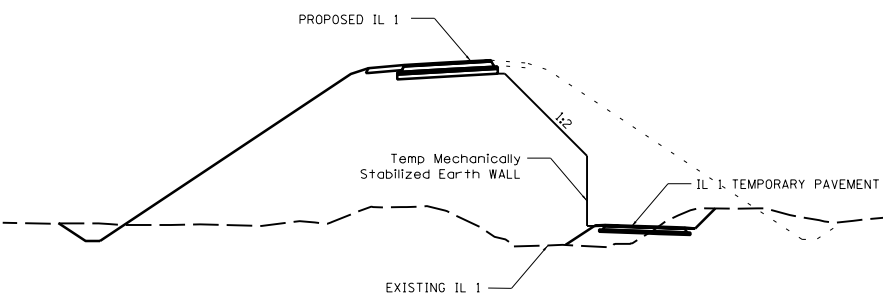

STAGE 2

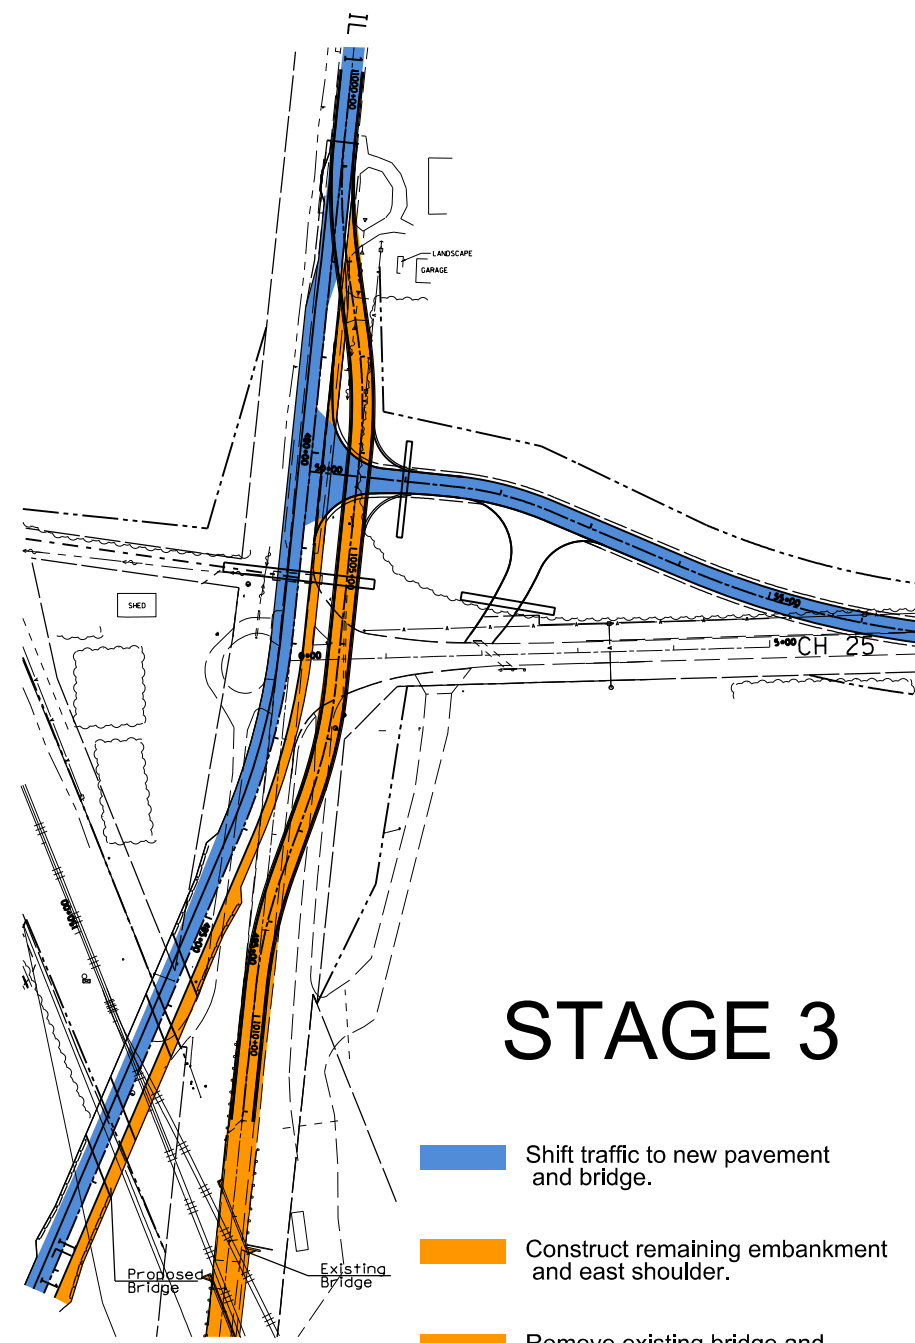

STAGE 3

- Shift traffic to new pavement and bridge.
- Construct remaining embankment and east shoulder.
- Remove existing bridge and fill viaduct.
- Maintain access to all driveways not being removed.
- Short term Railroad closure for removing bridge
